भारतीय रिज़र्व बैंक
संपदा विभाग, भोपाल

Programme Chart

Name of Work	Construction of additional quarters for staff/officers of Reserve Bank of India at Char Imli, Bhopal
NIT No	66/CE(Bhopal)/EE-I/2025-26
Agency	M/s B L Infra Projects Pvt Ltd
Estimated Cost	Rs. 126,63,30,074/-
Tender Amount	Rs. 102,98,12,931/-
Date of Start	15-06-2026
Stipulated date of completion	14-06-2028
Actual date of completion	-
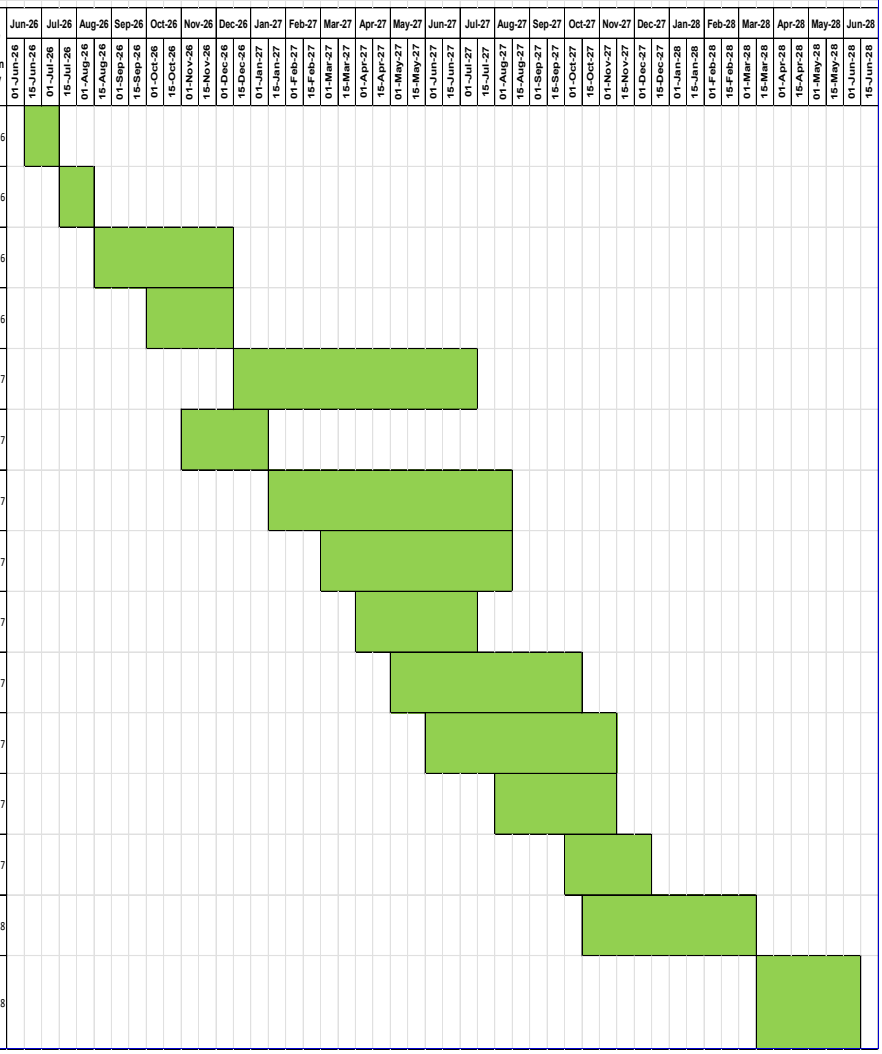
Sr No	Description	Date of start of activity	Tentative date of completion of activity
1	Demolishing, Disposal of C&D Waste, Temporary Barricading	15-06-2026	14-07-2026
2	Construction of site office, labour huts, submission of design mix, association of specilised agency, shuttering plan, BIM for MEP &	14-07-2026	14-08-2026
3	Excavation of foundation and RCC up to footing	15-08-2026	14-12-2026
4	Uploading all drawings and BIM in ERP, RCC up to plinth	01-10-2026	14-12-2026
5	RCC work in superstructure	15-12-2026	15-07-2027
6	Brick work in foundation	01-11-2026	15-01-2027
7	Brick work in superstructure	15-01-2027	15-08-2027
8	Door and Window frame	01-03-2027	14-08-2027
9	Internal water supply & plumbing & drainage	01-04-2027	15-07-2027
10	Plastering	01-05-2027	14-10-2027
11	Flooring	01-06-2027	14-11-2027
12	Finishing	01-08-2027	10-11-2027
13	Fixing door and window shutter	01-10-2027	14-12-2027
14	Testing of all buildings, road work, underground tank	14-10-2027	14-03-2028
15	Cleaning of all buildings and removal of all protective films, all development work including testing & commissioning and handover, completion certificate and fire clearance certificate	14-03-2028	14-06-2028
